


20190708 Kealakehe Schedule

ID	Task Name	Duration	Baseline Start	Baseline	Predecessors	Actual Start	Actual Finish	Est Start	Est Finish	2018	2019	2020	2021	2022	2023	2024
1	Baseline date	0 days	Mon 12/3/18	Mon 12/3/18		NA	NA	Mon 12/3/18	Mon 12/3/18		12/3					
3	<b>EIS</b>	<b>181 days?</b>	<b>Mon 12/3/18</b>	<b>Mon 8/12/19</b>		<b>Mon 12/3/18</b>	<b>NA</b>	<b>Mon 12/3/18</b>	<b>Mon 8/12/19</b>							
4	Develop administrative DEIS	2.8 wks	Mon 12/3/18	Fri 12/21/18		Mon 12/3/18	Thu 12/20/18	Mon 12/3/18	Thu 12/20/18		-1 day					
5	Submit administrative draft EIS	0 days	Fri 12/21/18	Fri 12/21/18	4	NA	NA	Thu 12/20/18	Thu 12/20/18		12/20					
6	Administrative DEIS County review	4.8 wks	Mon 12/24/18	Fri 12/28/18	5	Fri 12/21/18	Thu 1/24/19	Fri 12/21/18	Thu 1/24/19		19 days					
7	Update DEIS	7.6 wks	Mon 12/31/18	Fri 1/25/19	4	Fri 12/21/18	Tue 2/12/19	Fri 12/21/18	Tue 2/12/19		12 days					
8	Submit DEIS to OEQC	0 days	Fri 1/25/19	Fri 1/25/19	7	NA	NA	Tue 2/12/19	Tue 2/12/19		2/12					
9	OEQC publish date	0 days	Thu 2/7/19	Thu 2/7/19	8FS+8 days	NA	NA	Sat 2/23/19	Sat 2/23/19		2/23					
10	DEIS comment period	6.8 wks	Fri 2/8/19	Mon 3/25/19	9FS-1 day	Fri 2/22/19	Wed 4/10/19	Fri 2/22/19	Wed 4/10/19		12 days					
11	Offramp for separate EA for SAT	0 days	Mon 3/25/19	Mon 3/25/19	10	NA	NA	Wed 4/10/19	Wed 4/10/19		4/10					
12	Section 7 through DOH	8 wks	Mon 1/28/19	Fri 5/10/19	8	Sat 5/18/19	NA	Sat 5/18/19	Fri 7/12/19		45 days					
13	<b>Archeological Clearance and Section 106</b>	<b>466 days</b>	<b>Mon 1/28/19</b>	<b>Fri 5/10/19</b>	<b>8</b>	<b>Mon 3/4/19</b>	<b>NA</b>	<b>Mon 3/4/19</b>	<b>Mon 12/14/20</b>							
14	Submit preliminary archeo study for HRS	0 days	NA	NA		NA	NA	Mon 4/8/19	Mon 4/8/19		4/8					
15	SHPD review for HRS	52 wks	NA	NA	14	NA	NA	Mon 4/8/19	Fri 4/3/20		0 days					
16	DOH submit preliminary archeo study for Section 106	2 wks	NA	NA	14	NA	NA	Mon 4/8/19	Fri 4/19/19		0 days					
17	SHPD review for Section 106	52 wks	NA	NA	16	NA	NA	Mon 4/22/19	Fri 4/17/20		0 days					
18	AIIS proposal submitted	1 day	NA	NA		Mon 3/4/19	Mon 3/4/19	Mon 3/4/19	Mon 3/4/19		0 days					
19	COH contracting	8 wks	NA	NA	18	NA	NA	Tue 3/5/19	Mon 4/29/19		0 days					
20	Subcontracting	2 wks	NA	NA	19	NA	NA	Tue 4/30/19	Mon 5/13/19		0 days					
21	Draft AIS development	20 wks	NA	NA	20	NA	NA	Tue 5/14/19	Mon 9/30/19		0 days					
22	Draft AIS internal review	2 wks	NA	NA	21	NA	NA	Tue 10/1/19	Mon 10/14/19		0 days					
23	Submit draft AIS to SHPD	0 days	NA	NA	22	NA	NA	Mon 10/14/19	Mon 10/14/19		0 days					
24	SHPD review AIS	52 wks	NA	NA	23	NA	NA	Tue 10/15/19	Mon 10/12/20		10/14					
25	Finalize AIS based on SHPD comments and submit	2 wks	NA	NA	24	NA	NA	Tue 10/13/20	Mon 10/26/20		0 days					
26	DOH submits Section 106 letter of determination	1 wk	NA	NA	25	NA	NA	Tue 10/27/20	Mon 11/2/20		0 days					
27	30-day review period for SHPD	30 days	NA	NA	26	NA	NA	Tue 11/3/20	Mon 12/14/20		0 days					
28	Section 106 complete	0 days	NA	NA	27	NA	NA	Mon 12/14/20	Mon 12/14/20		0 days					
29	Develop draft FEIS	19 days	Tue 3/26/19	Mon 4/29/19	10,28	NA	NA	Tue 12/15/20	Fri 1/8/21		444 days					
30	Draft FEIS County review	2 wks	Tue 4/30/19	Mon 5/13/19	29	NA	NA	Mon 1/11/21	Fri 1/22/21		444 days					
31	Update FEIS	1 wk	Tue 5/14/19	Mon 5/27/19	30,12,13,24	NA	NA	Mon 1/25/21	Fri 1/29/21		439 days					
32	Submit FEIS and notice of determination to OEQC and Mayor	0 days	Mon 5/27/19	Mon 5/27/19	31	NA	NA	Fri 1/29/21	Fri 1/29/21		1/29					
33	OEQC publish date	0 days	Fri 6/7/19	Fri 6/7/19	32FS+9 days	NA	NA	Thu 2/11/21	Thu 2/11/21		2/11					
34	Construction contracting can begin (at risk)	0 days	Mon 6/10/19	Mon 6/10/19	33FS+3 days	NA	NA	Tue 2/16/21	Tue 2/16/21		2/16					
35	60 day legal challenge period	8.6 wks	Tue 6/11/19	Mon 8/12/19	34	NA	NA	Wed 2/17/21	Fri 4/16/21		439 days					
36	FEIS complete - all clear	0 days	Mon 8/12/19	Mon 8/12/19	35	NA	NA	Fri 4/16/21	Fri 4/16/21		4/16					
38	<b>USBR Title XVI Funding (**DRAFT**)</b>	<b>730 days</b>	<b>NA</b>	<b>NA</b>		<b>Mon 4/22/19</b>	<b>NA</b>	<b>Mon 4/22/19</b>	<b>Fri 2/4/22</b>							
39	<b>Application</b>	<b>81 days</b>	<b>NA</b>	<b>NA</b>		<b>Mon 4/22/19</b>	<b>NA</b>	<b>Mon 4/22/19</b>	<b>Mon 8/12/19</b>							
40	Submit application	1 day	NA	NA		Mon 4/22/19	Mon 4/22/19	Mon 4/22/19	Mon 4/22/19		0 days					
41	USBR review of application	16 wks	NA	NA	40	Mon 4/22/19	NA	Mon 4/22/19	Mon 8/12/19		0 days					
42	USBR authorization to do feasibility study	0 days	NA	NA	41	NA	NA	Mon 8/12/19	Mon 8/12/19		8/12					
43	<b>Feasibility study</b>	<b>365 days</b>	<b>NA</b>	<b>NA</b>		<b>NA</b>	<b>NA</b>	<b>Tue 4/23/19</b>	<b>Mon 9/14/20</b>							
44	Prepare feasibility study proposal	10 wks	NA	NA	40	NA	NA	Tue 4/23/19	Mon 7/1/19		0 days					
45	Contracting	6 wks	NA	NA	44	NA	NA	Tue 7/2/19	Mon 8/12/19		0 days					
46	Feasibility study NTP	0 days	NA	NA	45	NA	NA	Mon 8/12/19	Mon 8/12/19		8/12					
47	Prepare draft feasibility study	26 wks	NA	NA	46	NA	NA	Tue 8/13/19	Mon 2/10/20		0 days					
48	Submit draft feasibility study	0 days	NA	NA	47	NA	NA	Mon 2/10/20	Mon 2/10/20		2/10					
49	County review	2 wks	NA	NA	48	NA	NA	Tue 2/11/20	Mon 2/24/20		0 days					
50	Prepare final feasibility study	3 wks	NA	NA	49	NA	NA	Tue 2/25/20	Mon 3/16/20		0 days					
51	Submit final feasibility study to USBR	0 days	NA	NA	50	NA	NA	Mon 3/16/20	Mon 3/16/20		3/16					
52	USBR reviews feasibility study	26 wks	NA	NA	51	NA	NA	Tue 3/17/20	Mon 9/14/20		0 days					
53	USBR determines project is feasible	0 days	NA	NA	52	NA	NA	Mon 9/14/20	Mon 9/14/20		9/14					
54	<b>NEPA</b>	<b>325 days</b>	<b>NA</b>	<b>NA</b>		<b>NA</b>	<b>NA</b>	<b>Tue 2/11/20</b>	<b>Mon 5/10/21</b>							

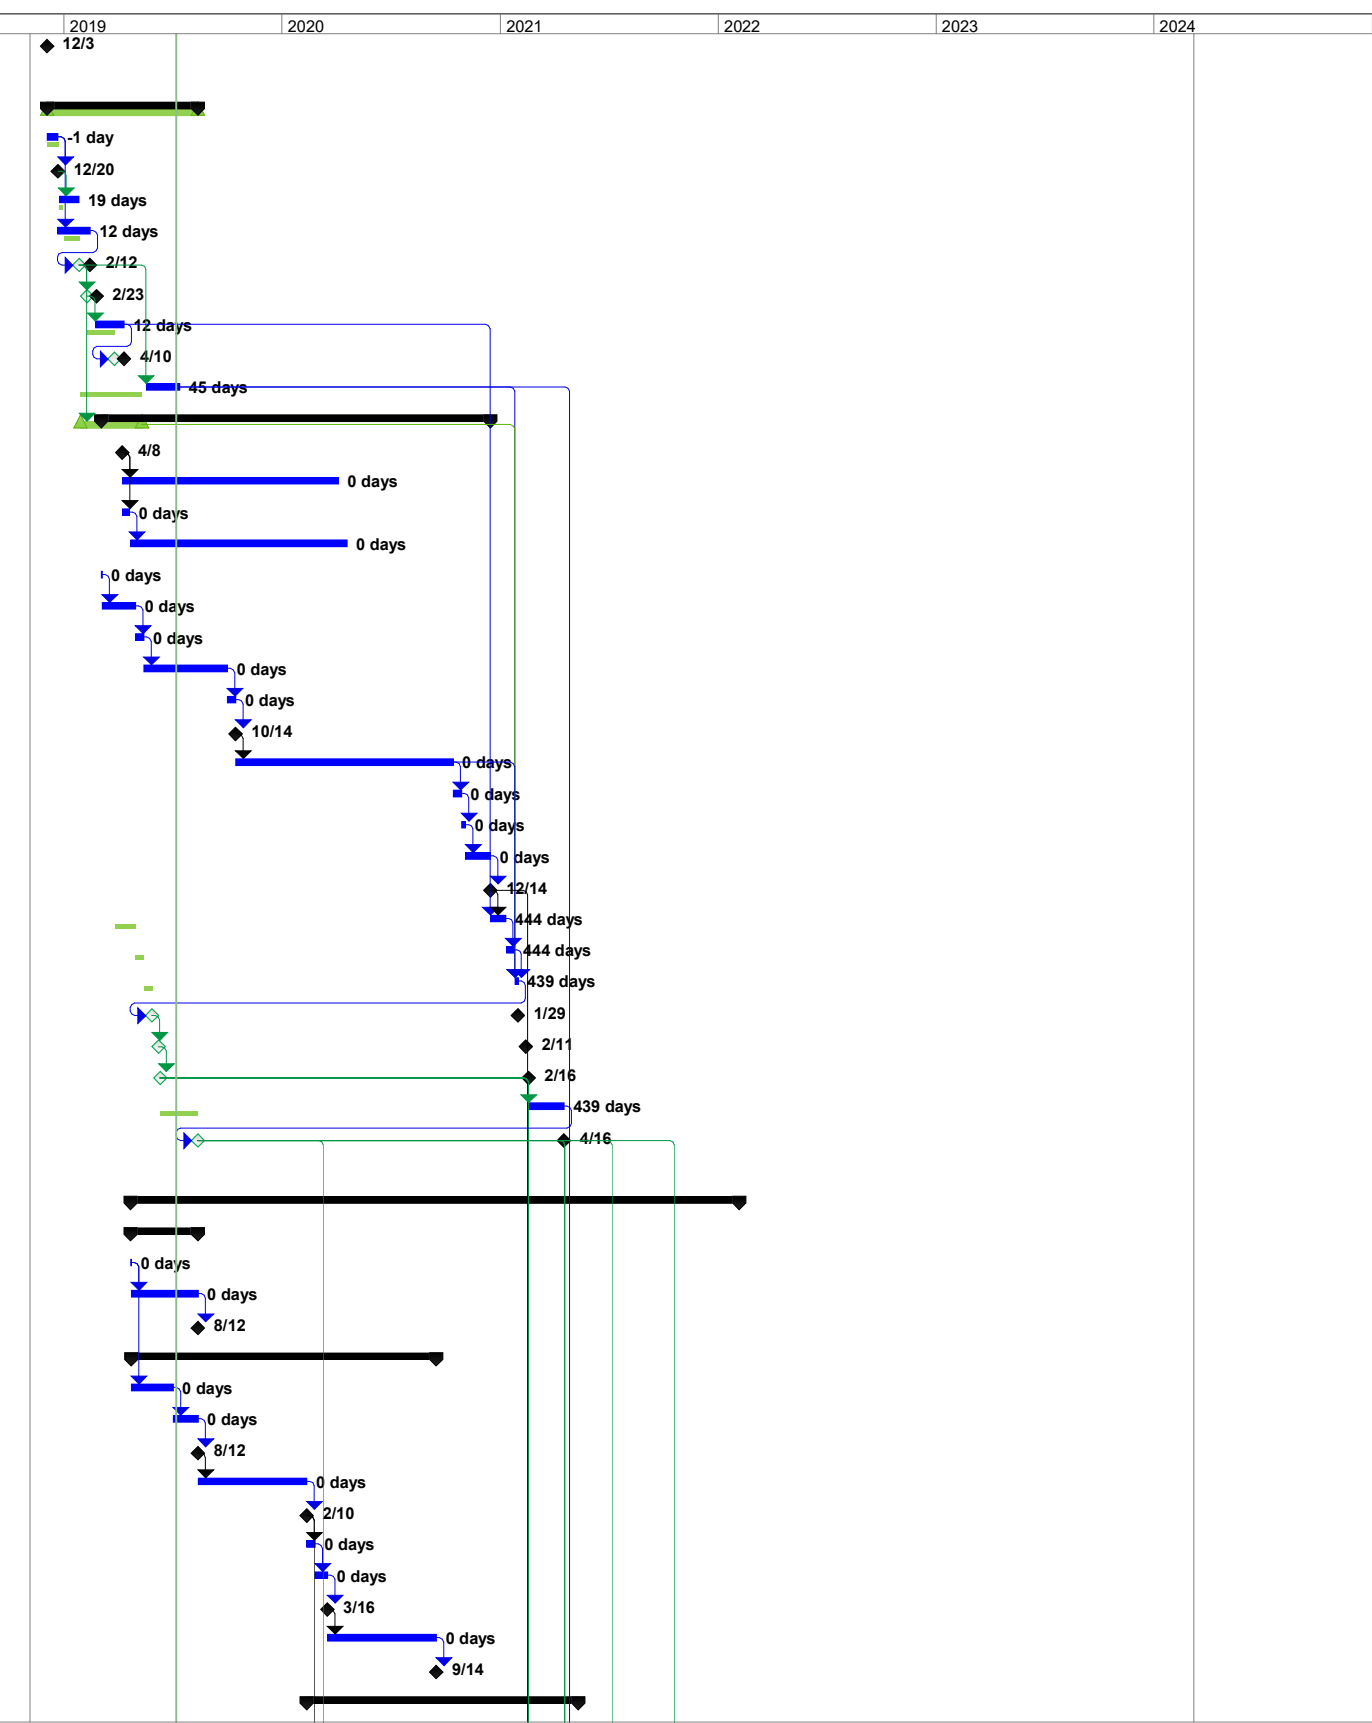

Project: Kealakehe Schedule  
Date: Mon 7/8/19

Baseline Milestone	◇	Task	▬	Start-only	┌	Baseline Split	⋯	Manual Summary	▬	External Milestone	◇	Inactive Summary	▬
Baseline Summary	▬	Split	⋯	Finish-only	┐	Milestone	◆	Project Summary	▬	Inactive Task	▬	Deadline	↓
Critical Progress	▬	Manual Task	▬	Duration-only	▬	Summary	▬	External Tasks	▬	Inactive Milestone	◇	Baseline	▬
